
DICKEY DR REPAVING PROJECT 07/23-07/30/15

7/23 Asphalt Milling • 7/24 Full Depth Reclamation • 7/25 No activity • 7/26 Proof Roll Test • 7/27 New Binder Course • 7/28 New Top Coat • 7/30 Striping & Clean Up DOBBS HAL Eagle Row WOODRUFF PF CENTER & TRACK **ROAD CLOSURE PEAVINE POINT & PARKING** CONSTRUCTION LOT **ROAD LIMITS CLOSURE POINT &** CONSTRUCTION **LIMITS Building/PAIS LOADING DOCK** Eagle Row **AND PEDESTRIAN CROSSWALKS TO REMAIN** ATWOOD CHEMISTRY CENTER **ACCESSIBLE** PROJECT NOTES: TRAFFIC FLOW ON DICKEY DRIVE: • TWO-WAY TRAFFIC ALLOWED WHEN CONSTRUCTION ACTIVITIES END FROM 7 PM > 7 AM **QUADRANGLE** ALL TRAFFIC WILL BE DIRECTED WHEN LIMITED TO ONE SIDE PASSING (The Quad) Cross Walks Site Fencing Repaying Area ©2015 Emory University, Planning Design & Construction, All Rights Reserved

EAGLE ROW REPAVING PROJECT 07/23-7/30/15

7/23 Asphalt Milling • 7/24 Full Depth Reclamation • 7/25 No activity • 7/26 Proof Roll Test • 7/27 New Binder Course • 7/28 New Top Coat • 7/30 Striping & Clean Up

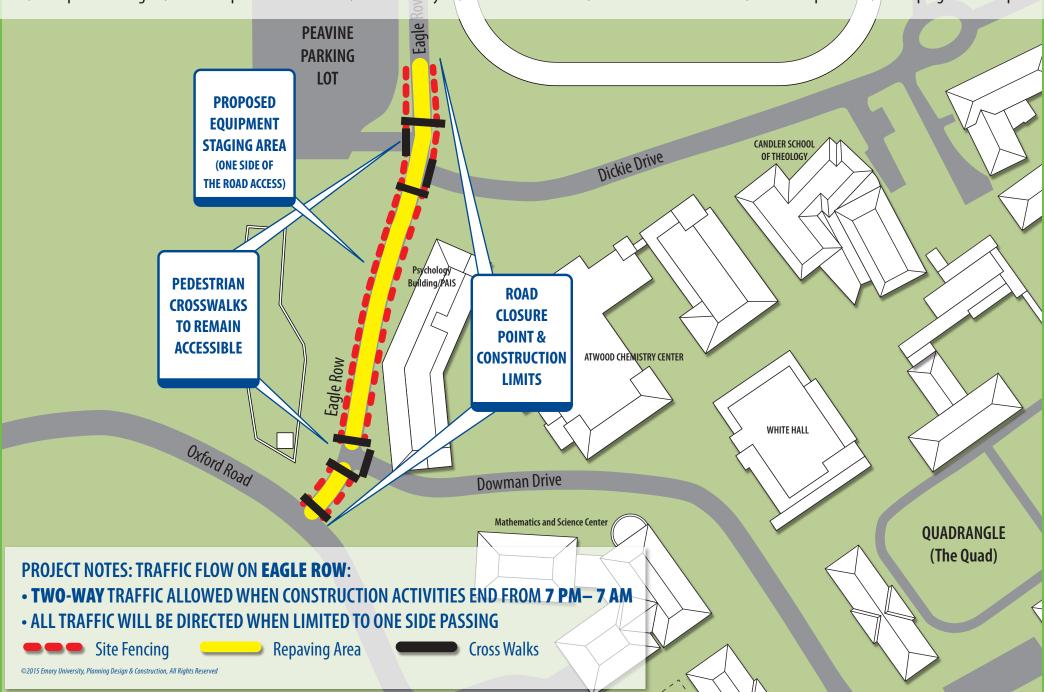

DOWMAN DR REPAVING PROJECT 07/24-7/30/15

